



WEEKLY CONSTRUCTION UPDATE

Project Title: Whitman 20-Inch Force Main Replacement CWSRF - 6885		Report #: EP - 08-19-2022
Project Location: Brockton, MA and Whitman, MA	From: 8/15/2022	Week: 18
Client: Whitman, MA	To: 8/19/2022	Engineer Project #: 279-1901
On-Site Engineer: Bob Fitzgerald, Environmental Partners	Contact: (508) 776-7556	
Contractor: C. Naughton Corp.		

CONSTRUCTION ACTIVITIES COMPLETED THIS WEEK:

1. C. Naughton had one crew continuing the sewer force main installation on Auburn Street. C. Naughton installed approximately 600 LF of new 20-inch PVC sewer force main along Auburn Street. Approximately 80% of the sewer force main is complete on Auburn Street.
2. C. Naughton had a second crew continuing the installation of the water main on Auburn Street. C. Naughton installed approximately 900 LF of the new 12-inch DI water main and two 6-inch water main gate valves on Auburn Street. Approximately 40% of the water main is complete on Auburn Street.
3. C. Naughton completed several test pits along Auburn Street via vacuum excavation to verify the location of existing utilities.
4. C. Naughton detoured traffic onto Beaver Street and Alger Street while the sewer main work was on-going this week. A copy of the detour plan is attached for reference.
5. All trenches will be backfilled, compacted, and paved prior to leaving for the weekend.

WEEK LOOK-AHEAD SCHEDULE:

1. C. Naughton will have two crews on site next week (week of 8/22/2022) to continue installation of both the 20-inch PVC sewer force main and 12-inch DI water main on Auburn Street.
2. C. Naughton will have a third crew on-site on Monday 8/22 to begin installation of the new 20-inch HDPE sewer force main within the cross-country easement. Work is anticipated to begin in the cross-country easement between Auburn Street in Whitman and Alger Street in Brockton.

3. C. Naughton is maintaining a detour of Auburn Street while water and sewer work is on-going. C. Naughton will maintain access for local residents and for emergency vehicles while the detour is on-going.
4. Daily traffic updates to the Town's project website will be posted to alert residents of anticipated road closures and detours.

PROJECT PHOTOS



Photo 1: Installation of 12-inch DI Water Main on Auburn Street




Photo 2: Temporary Paving of the Sewer Trench on Auburn Street



Photo 3: Installation of a 6-inch Water Main Gate Valve on Auburn Street

Prepared By: Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC
Reviewed By: Andrew Grota, Project Manager, Environmental Partners Group, LLC

ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.

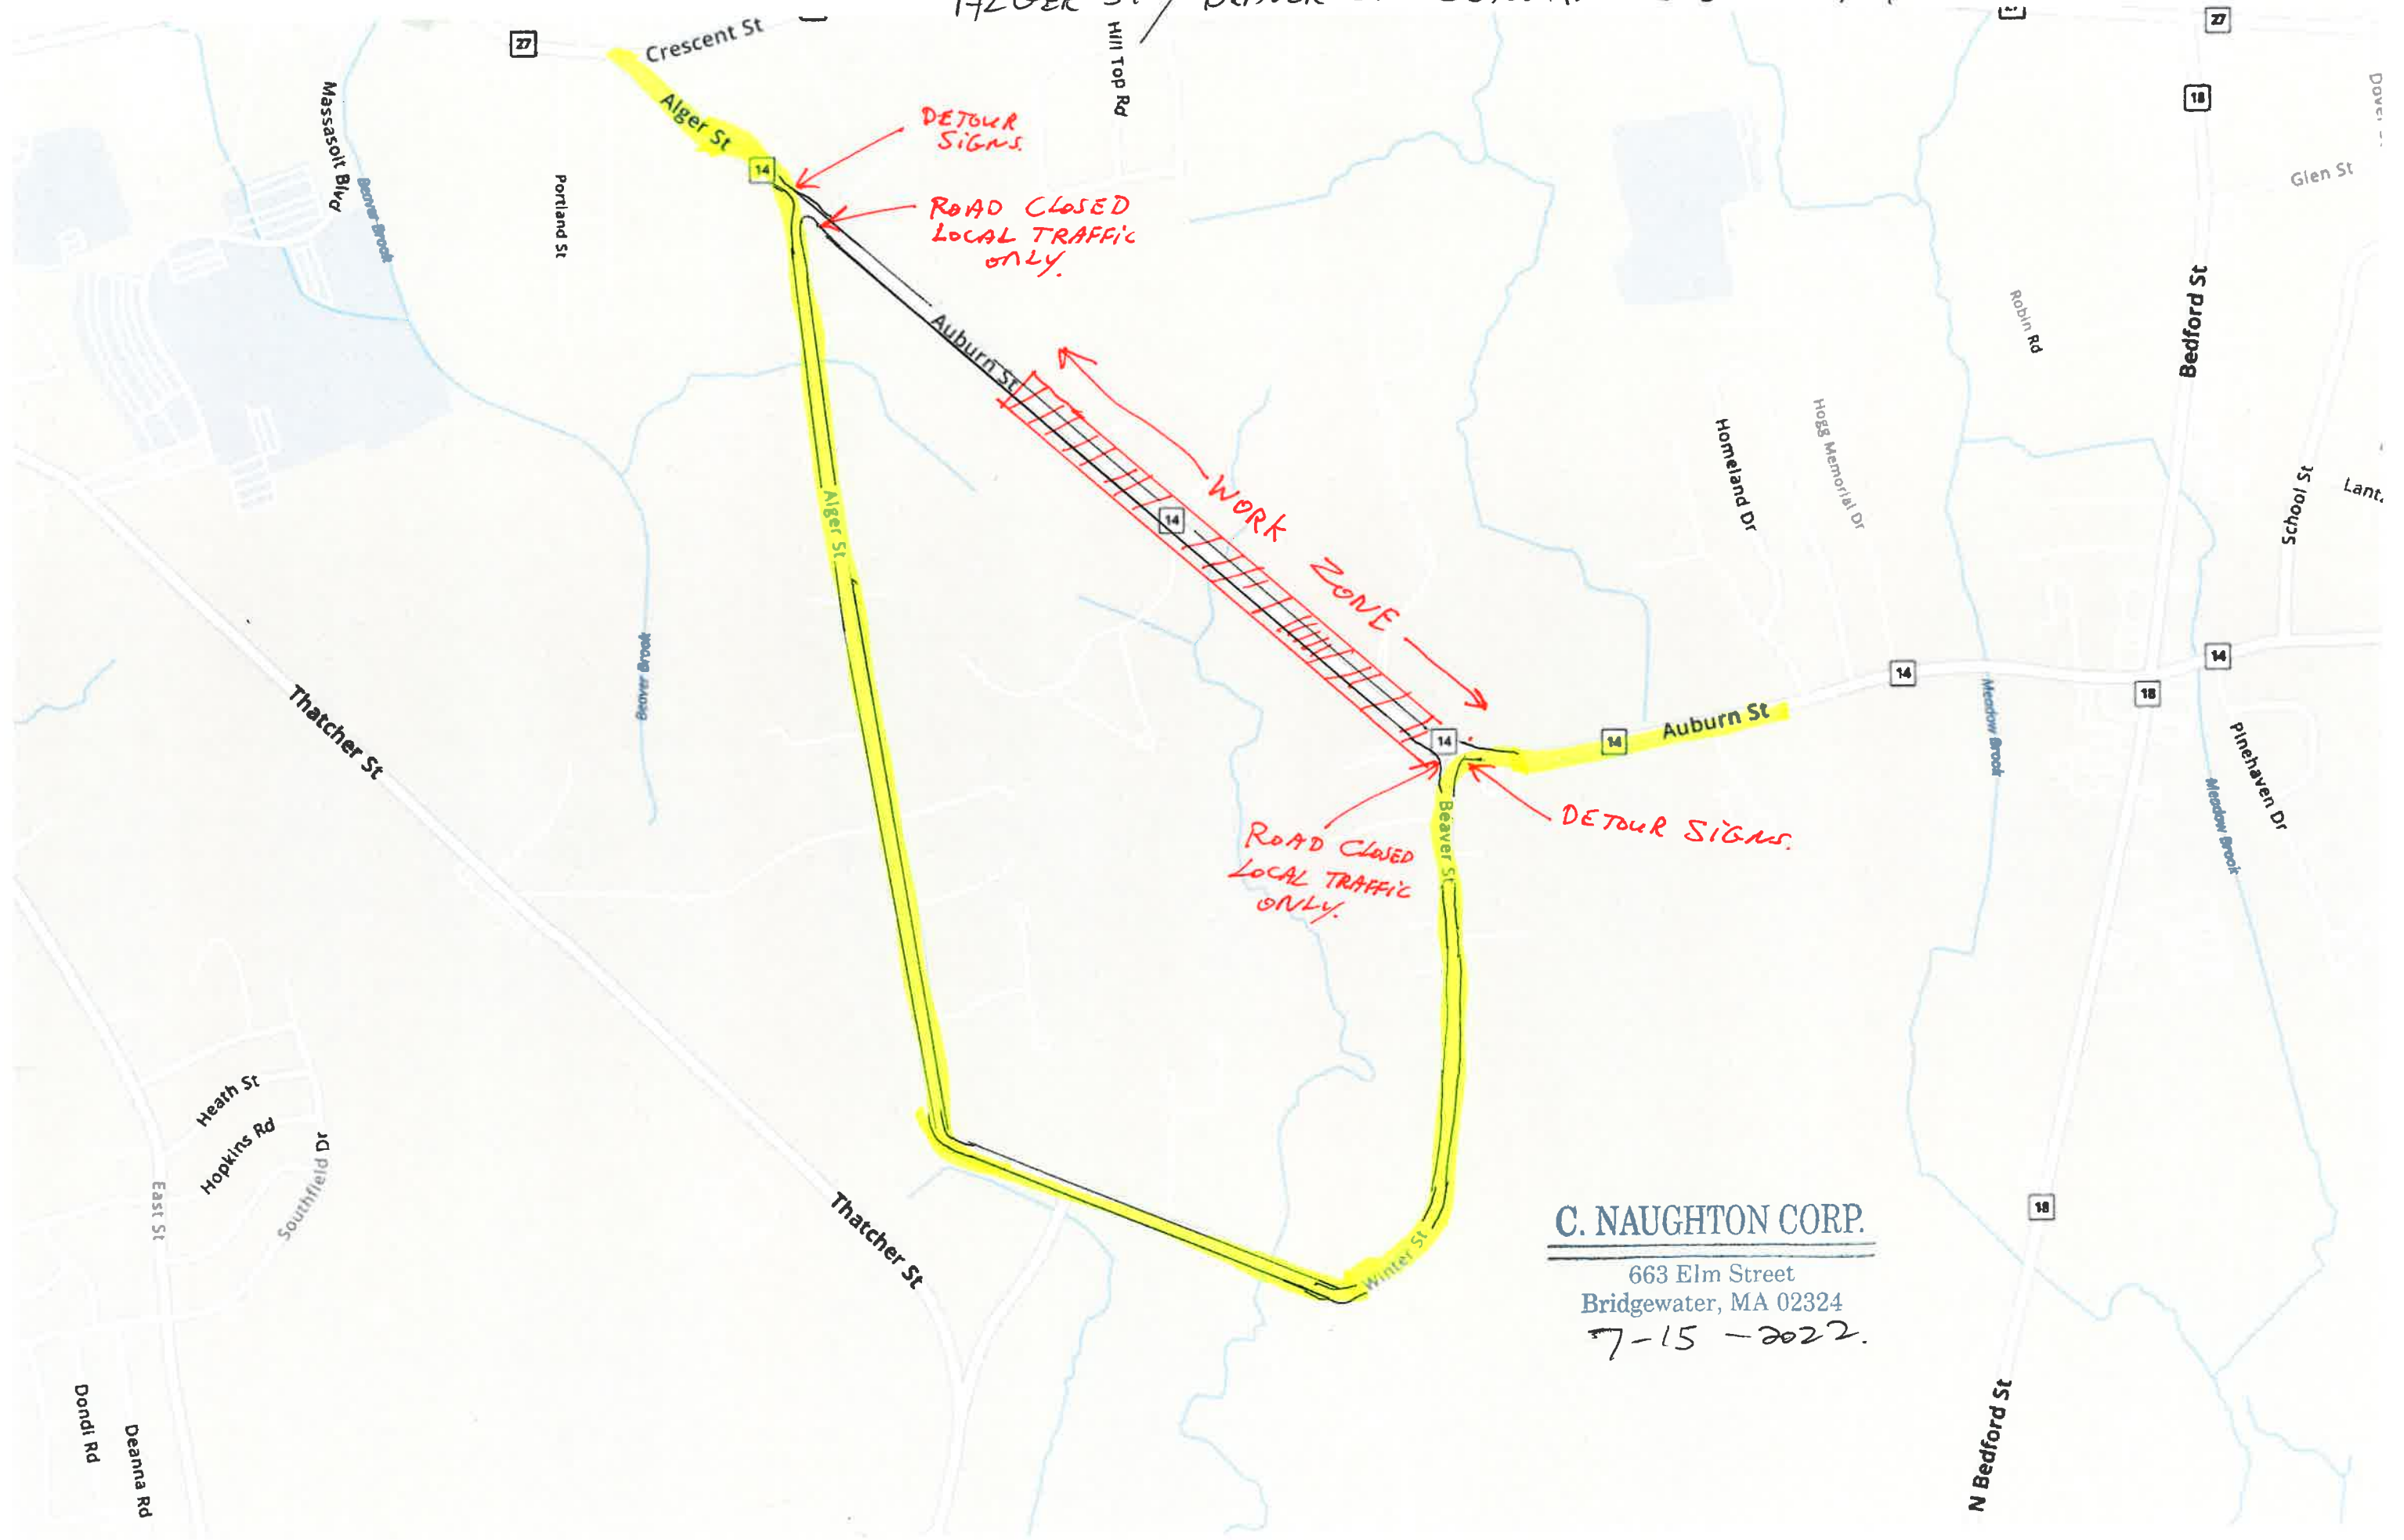

C. NAUGHTON CORP.
663 Elm Street
Bridgewater, MA 02324
7-15-2022.
