



## DAILY WORK & TRAFFIC UPDATE


<b>Project Title:</b> Whitman 20-Inch Force Main Replacement CWSRF - 6885	<b>Date:</b> 8-24-2022
<b>Construction Location:</b> Auburn Street, Whitman, MA	<b>Construction hours:</b> 7 A.M – 5 P.M.

### ANTICIPATED WORK SCHEDULE AND TRAFFIC MANAGEMENT:

1. C. Naughton has one crew installing the 20" PVC sewer force main on Auburn Street today towards Alger Street.
2. C. Naughton has another crew beginning the installation of the 20" HDPE sewer force main in the cross-country easement between Auburn Street in Whitman and Alger Street in Brockton.
3. Auburn Street will be closed in between Alger Street and Beaver Street for the installation of the 20" sewer force main, other than for local traffic and emergency vehicles. Traffic Management Plans showing the detour routes is attached.
4. Work is expected to take place from 7:00 a.m. until 5:00 p.m. All trenches will be backfilled and paved before leaving for the day.
5. Please note, the emergency access gate located at the rear of the middle school parking lot is closed for public access.

**Prepared By:** Amanda Shanahan, Project Engineer, Environmental Partners Group, LLC  
**Reviewed By:** Andrew Grota, Project Manager, Environmental Partners Group, LLC

ALGER ST / BEAVER ST DETOUR. BEGINS 7-18-2022.

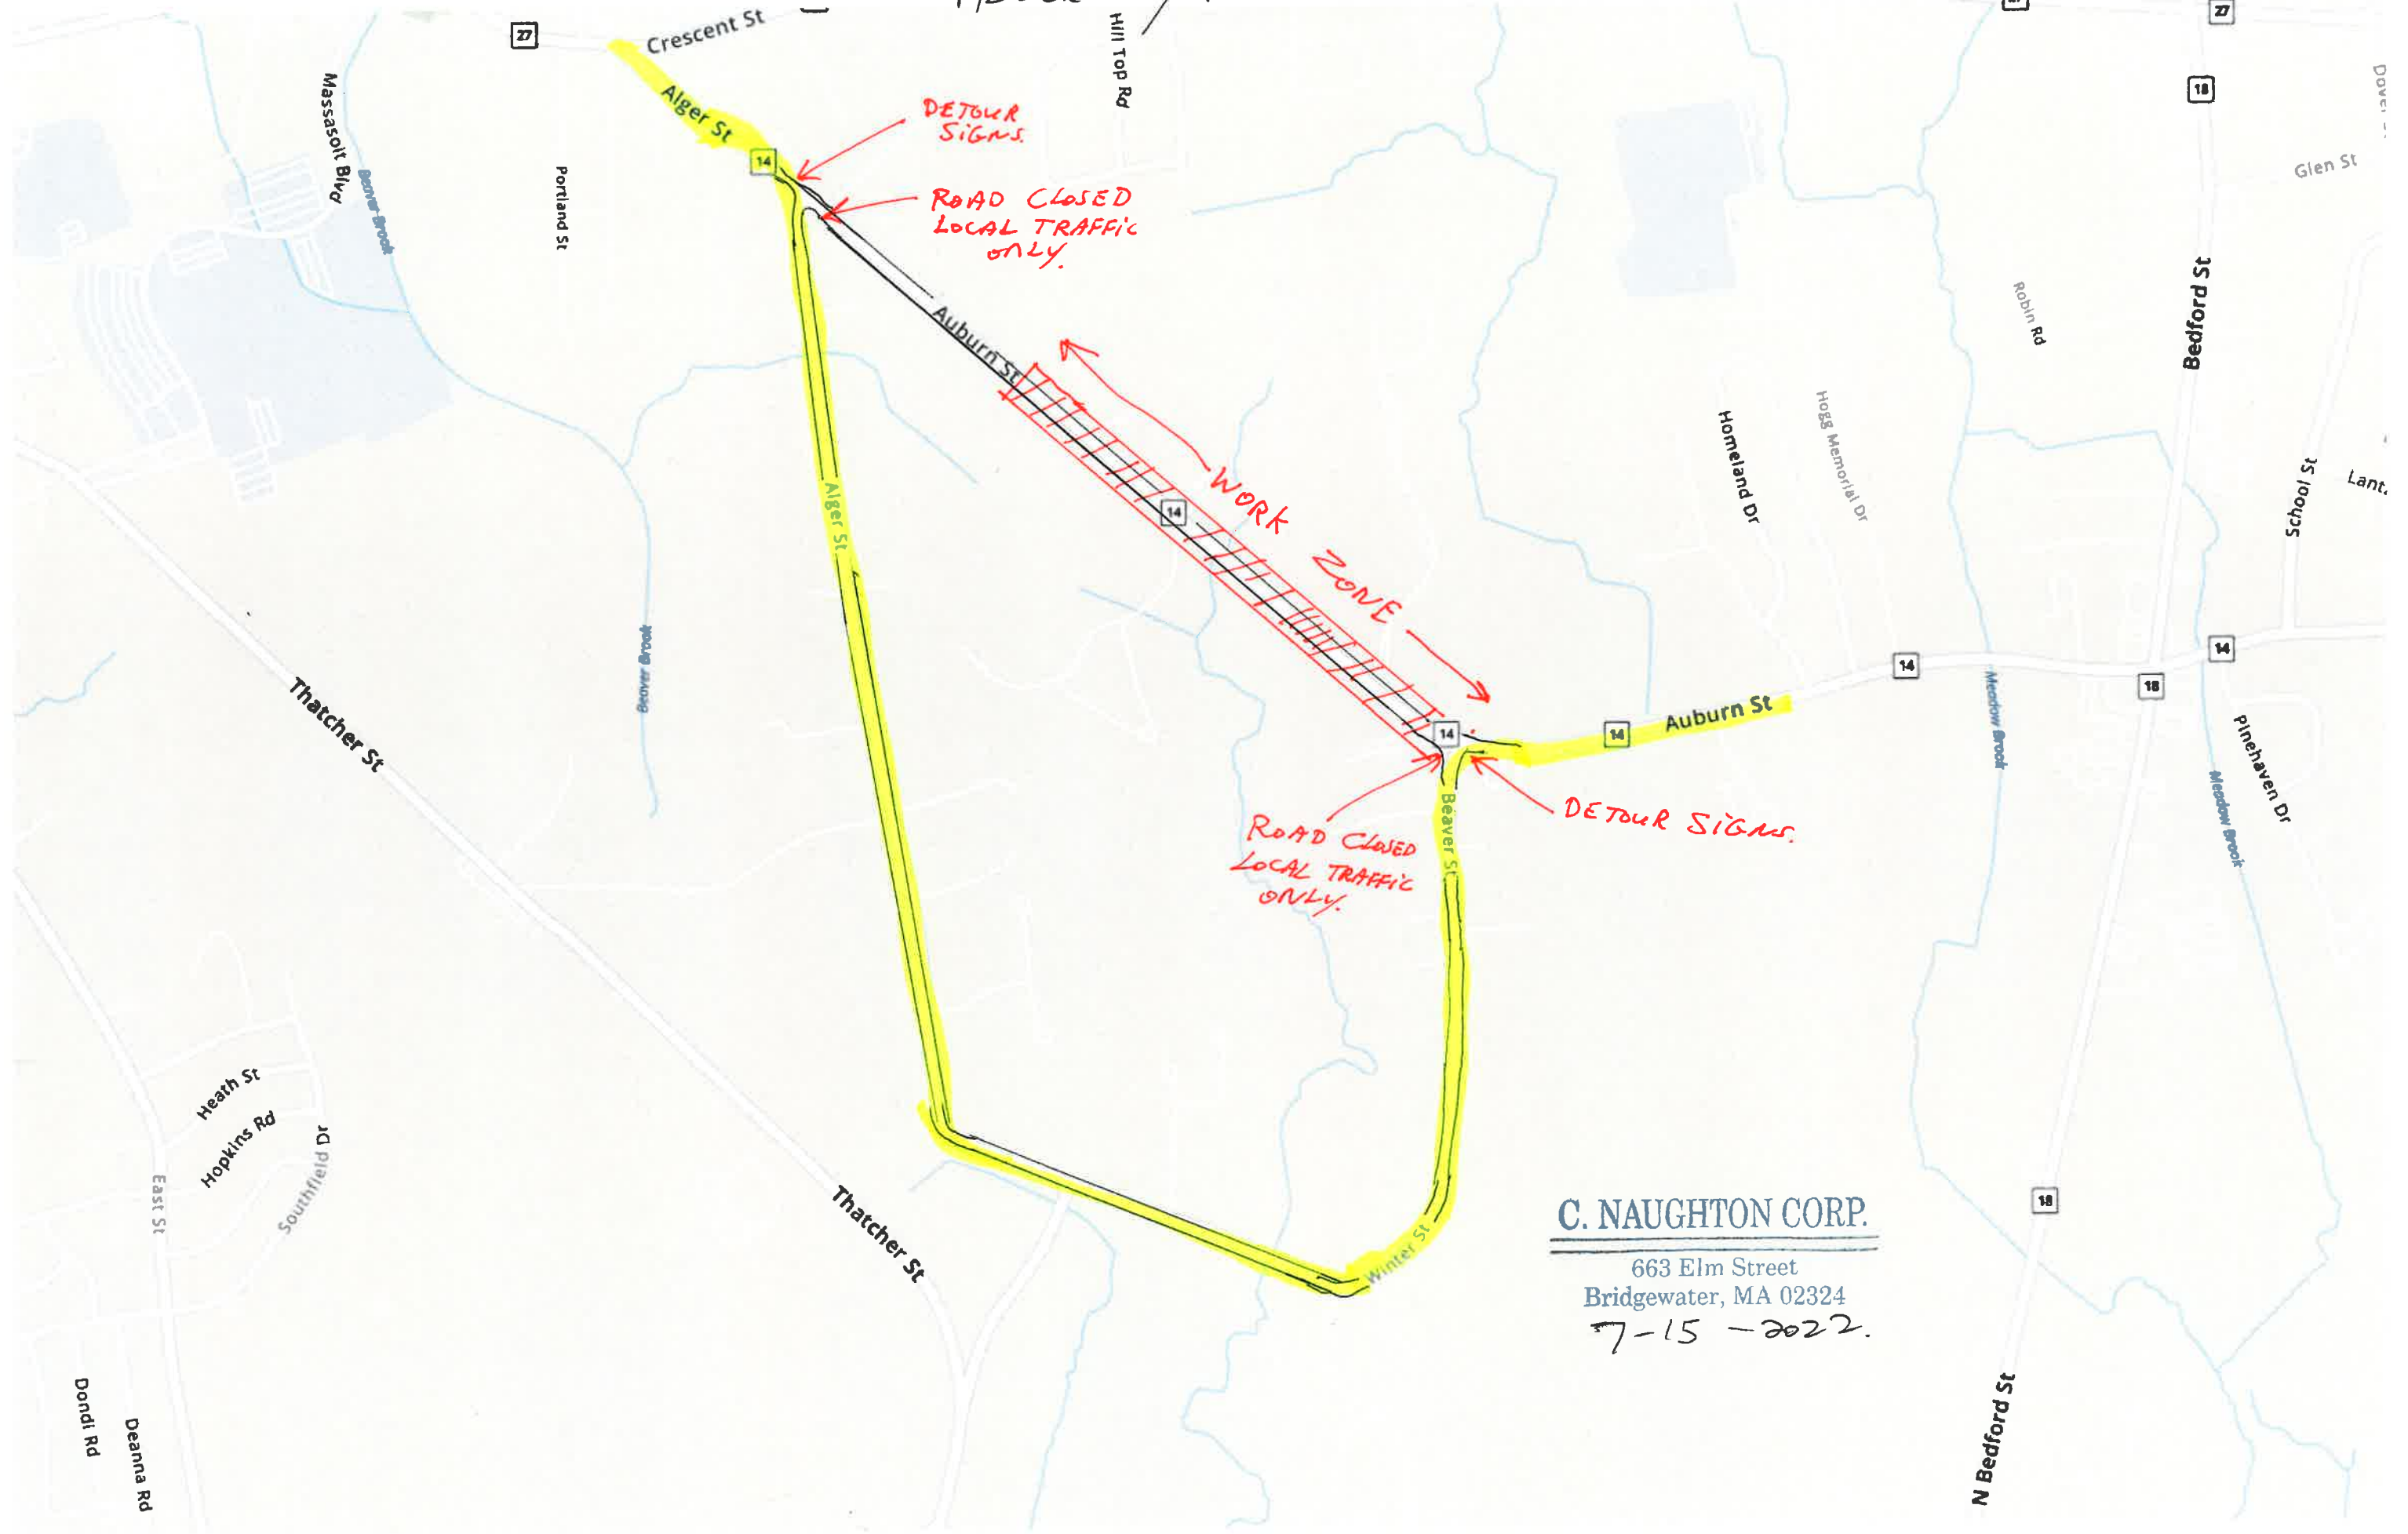

**C. NAUGHTON CORP.**  
663 Elm Street  
Bridgewater, MA 02324  
7-15-2022.
