



## WEEKLY CONSTRUCTION UPDATE

<b>Project Title:</b> Whitman 20-Inch Force Main Replacement CWSRF - 6885		<b>Report #:</b> EP - 11-11-2022
<b>Project Location:</b> Brockton, MA and Whitman, MA	<b>From:</b> 11/7/2022	<b>Week:</b> 30
<b>Client:</b> Whitman, MA	<b>To:</b> 11/11/2022	<b>Engineer Project #:</b> 279-1901
<b>On-Site Engineer:</b> Bob Fitzgerald, Environmental Partners	<b>Contact:</b> (508) 776-7556	
<b>Contractor:</b> C. Naughton Corp.		

### CONSTRUCTION ACTIVITIES COMPLETED THIS WEEK:

1. C. Naughton had one crew continuing the installation of the 20-inch PVC sewer force main on Southfield Drive in Brockton this week. C. Naughton installed approximately 320 LF of the new 20-inch PVC sewer force main and associated fittings along the roadway. The water main on Southfield Drive was temporarily shut down by Brockton Water Department on Wednesday 11/9 and Thursday 11/10 in order to complete the sewer main installation work.
2. C. Naughton had a second crew continuing the installation of the new 20-inch HDPE sewer force main in the cross-country easement off Thatcher Street. On Monday 11/7, C. Naughton installed approximately 200 LF of the new 20-inch HDPE sewer force main and associated fittings within the easement. On Tuesday 11/8, this crew moved over to the cross-country easement off Auburn Street in Whitman to begin the installation of the new meter pit assembly, which continued through the rest of the week.
3. Work is scheduled to continue on Friday 11/11 on both ends of the project. Additionally, C. Naughton will have a third crew restoring the temporary trench on Auburn Street on Friday 11/11 (from Beaver Street to Brockton/Whitman Town Line). All areas will be backfilled, compacted, and paved (on Southfield Drive) prior to leaving for the weekend.

### WEEK LOOK-AHEAD SCHEDULE:


1. C. Naughton will have two crews (at a minimum) on site next week (week of 11/14/2022): one crew one crew finishing the installation of the 20-inch PVC sewer force main on Southfield Drive and one crew continuing the installation of the new meter pit assembly off Auburn Street.
2. It is anticipated that the work on Southfield Drive will finish by early next week. The sewer force main installation work on Thatcher Street is expected to start during the middle of next week. A traffic detour plan for the work on Thatcher Street is attached to this email. Work on Thatcher Street is expected to take place through November 30<sup>th</sup>.

- Daily traffic updates to the Town's project website will be posted to alert residents of anticipated road closures and detours.

## PROJECT PHOTOS



*Photo 1: Start of Meter Pit Installation in Cross-Country Easement off Auburn Street*

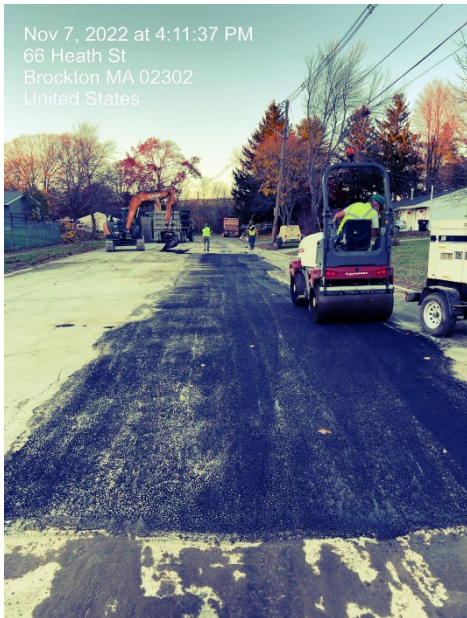


*Photo 2: Paving of Sewer Trench on Southfield Drive*



*Photo 3: Installation of New 20-Inch Sewer Force Main in Cross-Country Easement*

**Prepared By:** Andrew Grotz, Project Manager, Environmental Partners Group, LLC

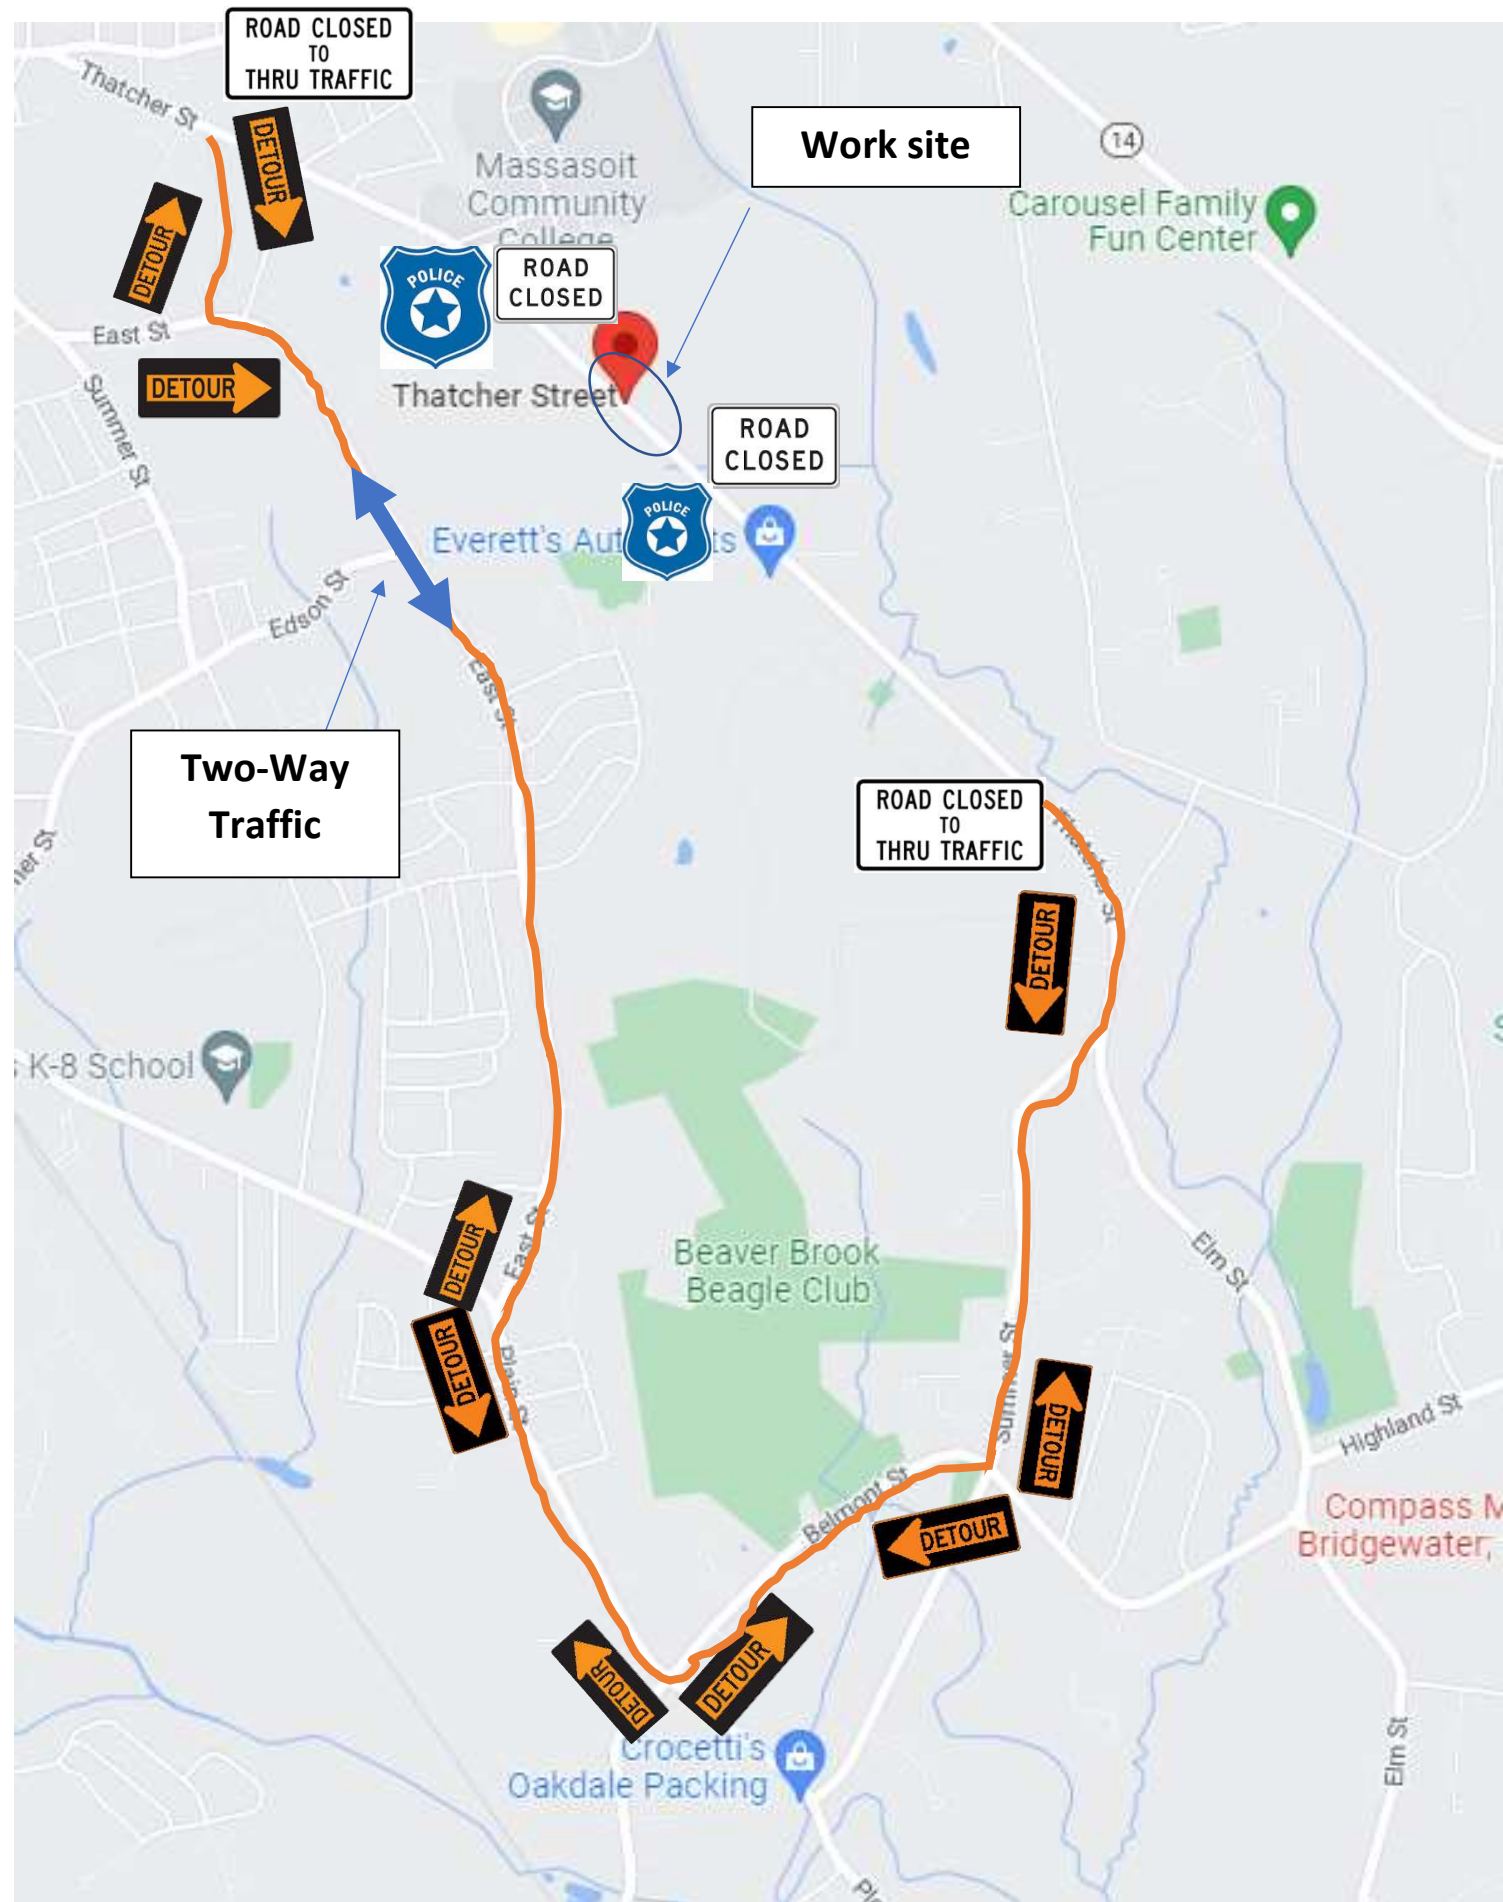

1. All construction signs per MassDOT MUTCD.
2. Work hours shall be 7am to 5pm.
3. C. Naughton Corp to order police details.

