



WEEKLY CONSTRUCTION UPDATE

Project Title: Whitman 20-Inch Force Main Replacement CWSRF - 6885		Report #: EP - 11-23-2022
Project Location: Brockton, MA and Whitman, MA	From: 11/21/2022	Week: 32
Client: Whitman, MA	To: 11/25/2022	Engineer Project #: 279-1901
On-Site Engineer: Bob Fitzgerald, Environmental Partners	Contact: (508) 776-7556	
Contractor: C. Naughton Corp.		

CONSTRUCTION ACTIVITIES COMPLETED THIS WEEK:

1. C. Naughton had one crew continue the installation of the 20-inch PVC sewer force main on Thatcher Street on Monday 11/21. Approximately 40 ft of pipe was installed. On Tuesday 11/22, C. Naughton coordinated with the Brockton Water Department on a temporary shutdown of the existing 12-inch CI water main in order to install a new gate valve and cross underneath the water main. Traffic was detoured while work was on-going this past week (refer to the attached traffic detour plan).
2. C. Naughton had a second crew backfilling and cleaning up their staging area off Auburn Street on Monday 11/21. The crew plans on heading back over to the cross-country easement off Thatcher Street on Monday 11/28 to continue the installation of the 20-inch HDPE sewer force main.
3. No work occurred on Wednesday 11/23, Thursday 11/24 or Friday 11/25. All areas were backfilled, compacted, and paved (on Thatcher Street) prior to leaving for the weekend.

WEEK LOOK-AHEAD SCHEDULE:

1. C. Naughton will have two crews (at a minimum) on site next week (week of 11/28/2022): one crew continuing the installation of the 20-inch HDPE sewer force main in the cross-country easement off Thatcher Street and one crew finishing the installation of the 20-inch PVC sewer force main on Thatcher Street.
2. A traffic detour plan for the work on Thatcher Street is attached to this email. Work on Thatcher Street is expected to take place through November 30th.

PROJECT PHOTOS

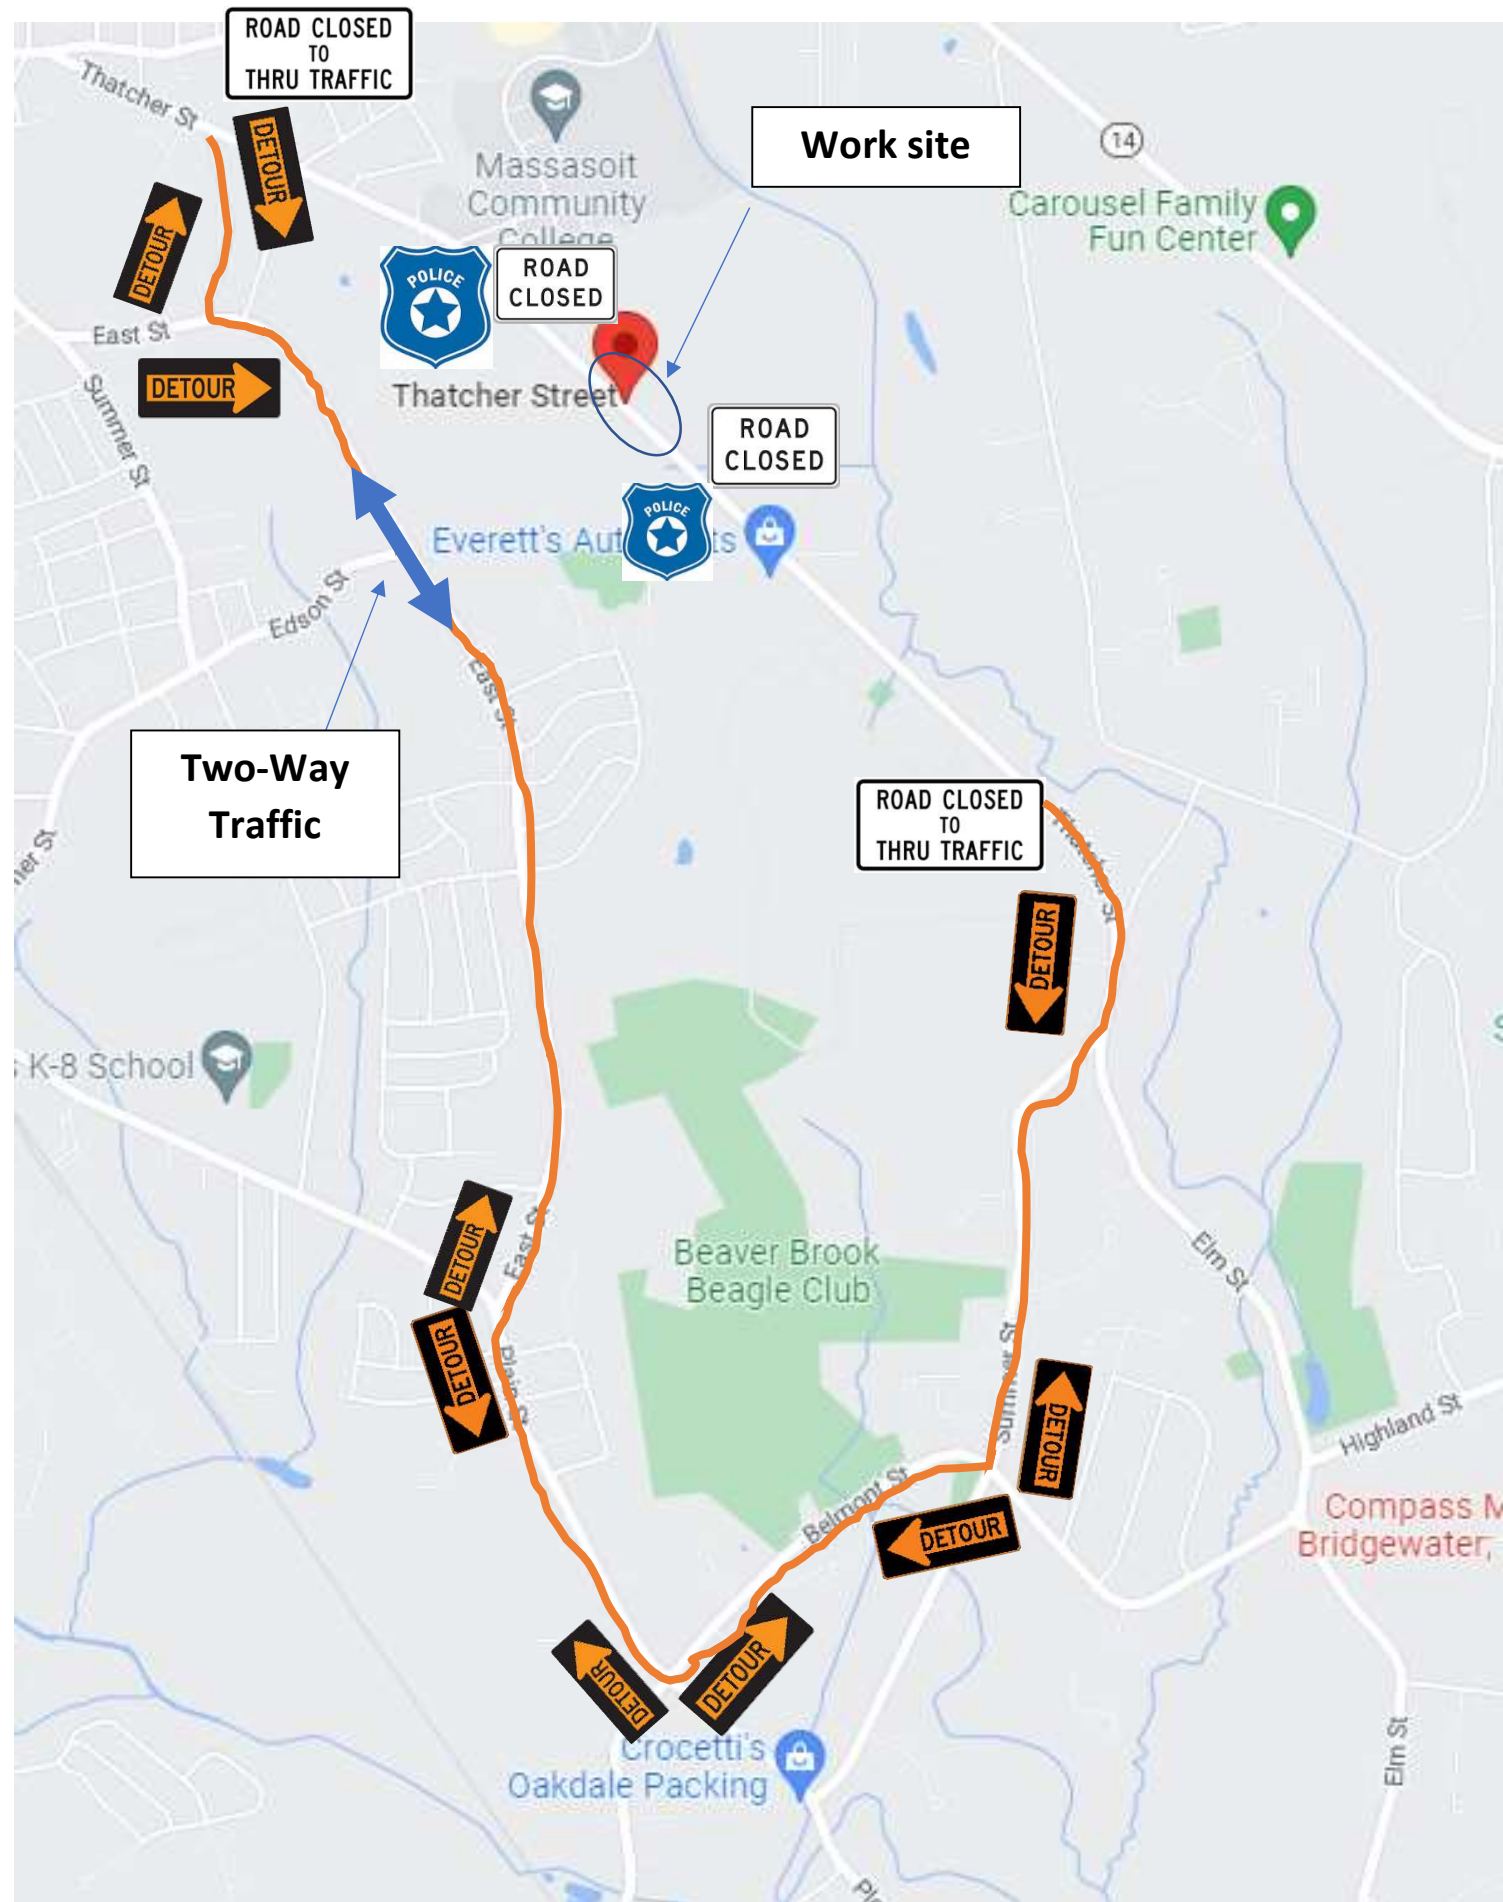


Photo 1: Cleanup in Easement off Auburn Street



Photo 2: Work Zone Secured with Fencing near Meter Pit

Prepared By: Andrew Grota, Project Manager, Environmental Partners Group, LLC



1. All construction signs per MassDOT MUTCD.
2. Work hours shall be 7am to 5pm.
3. C. Naughton Corp to order police details.

